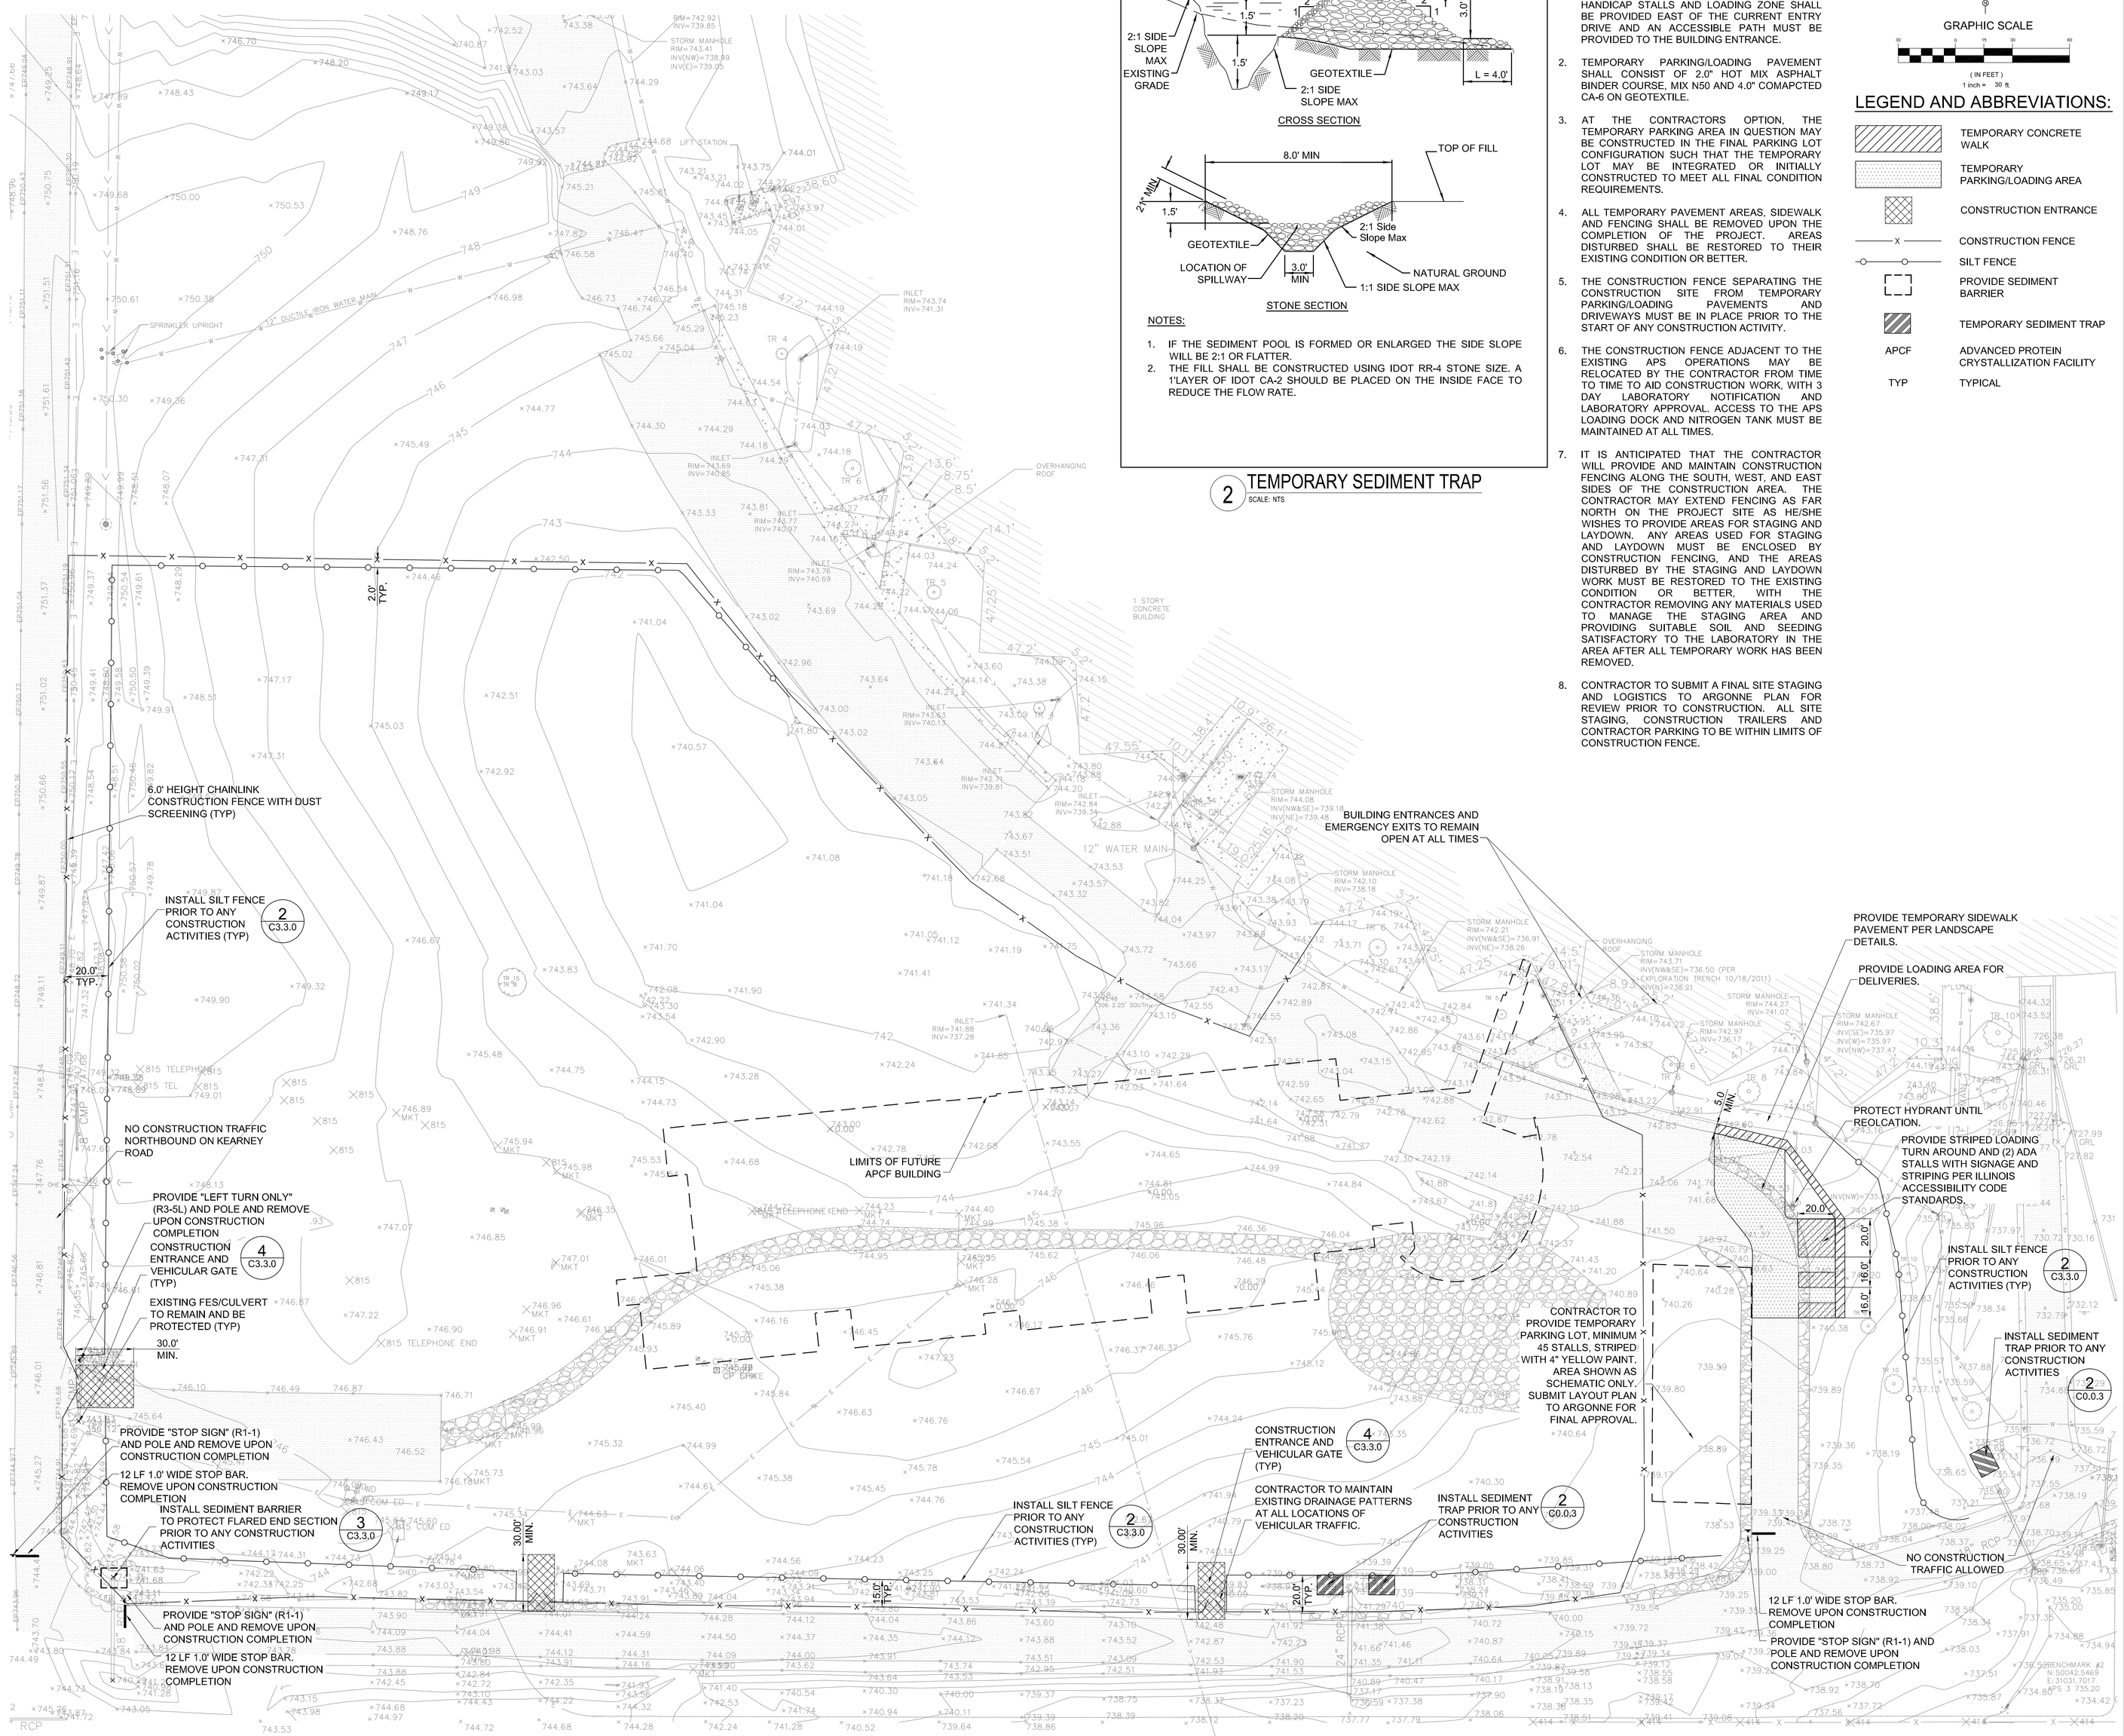

1 SITE STAGING PLAN
SCALE: 1" = 30'

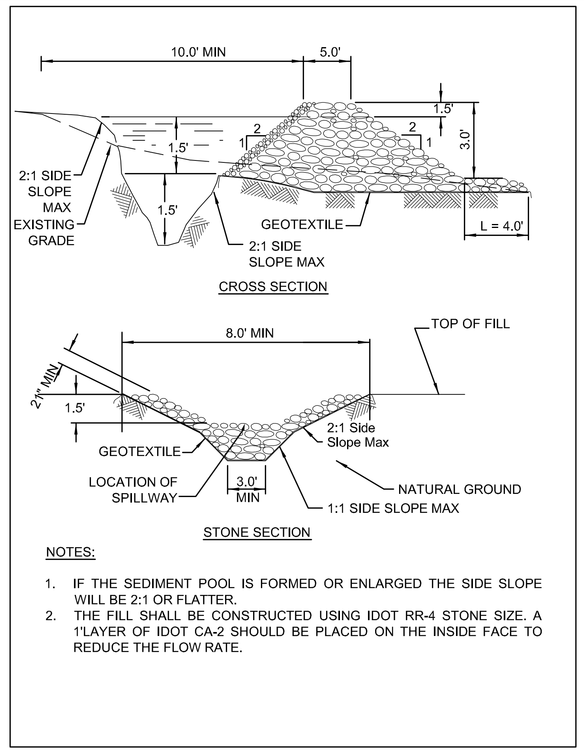

NOTES:

1. IF THE SEDIMENT POOL IS FORMED OR ENLARGED THE SIDE SLOPE WILL BE 2:1 OR FLATTER.
2. THE FILL SHALL BE CONSTRUCTED USING IDOT RR-4 STONE SIZE. A 1'LAYER OF IDOT CA-2 SHOULD BE PLACED ON THE INSIDE FACE TO REDUCE THE FLOW RATE.

2 TEMPORARY SEDIMENT TRAP
SCALE: NTS

STAGING NOTES:

1. BEFORE ASPHALT PARKING AREA AND WALKS ENTERING LOM 435 ARE REMOVED AN EQUIVALENT PAVED AREA MUST BE PROVIDED. HANDICAP STALLS AND LOADING ZONE SHALL BE PROVIDED EAST OF THE CURRENT ENTRY DRIVE AND AN ACCESSIBLE PATH MUST BE PROVIDED TO THE BUILDING ENTRANCE.
2. TEMPORARY PARKING/LOADING PAVEMENT SHALL CONSIST OF 2.0" HOT MIX ASPHALT BINDER COURSE, MIX N50 AND 4.0" COMAPCTED CA-6 ON GEOTEXTILE.
3. AT THE CONTRACTORS OPTION, THE TEMPORARY PARKING AREA IN QUESTION MAY BE CONSTRUCTED IN THE FINAL PARKING LOT CONFIGURATION SUCH THAT THE TEMPORARY LOT MAY BE INTEGRATED OR INITIALLY CONSTRUCTED TO MEET ALL FINAL CONDITION REQUIREMENTS.
4. ALL TEMPORARY PAVEMENT AREAS, SIDEWALK AND FENCING SHALL BE REMOVED UPON THE COMPLETION OF THE PROJECT. AREAS DISTURBED SHALL BE RESTORED TO THEIR EXISTING CONDITION OR BETTER.
5. THE CONSTRUCTION FENCE SEPARATING THE CONSTRUCTION SITE FROM TEMPORARY PARKING/LOADING PAVEMENTS AND DRIVEWAYS MUST BE IN PLACE PRIOR TO THE START OF ANY CONSTRUCTION ACTIVITY.
6. THE CONSTRUCTION FENCE ADJACENT TO THE EXISTING APS OPERATIONS MAY BE RELOCATED BY THE CONTRACTOR FROM TIME TO TIME TO AID CONSTRUCTION WORK, WITH 3 DAY LABORATORY NOTIFICATION AND LABORATORY APPROVAL. ACCESS TO THE APS LOADING DOCK AND NITROGEN TANK MUST BE MAINTAINED AT ALL TIMES.
7. IT IS ANTICIPATED THAT THE CONTRACTOR WILL PROVIDE AND MAINTAIN CONSTRUCTION FENCING ALONG THE SOUTH, WEST, AND EAST SIDES OF THE CONSTRUCTION AREA. THE CONTRACTOR MAY EXTEND FENCING AS FAR NORTH ON THE PROJECT SITE AS HE/SHE WISHES TO PROVIDE AREAS FOR STAGING AND LAYDOWN. ANY AREAS USED FOR STAGING AND LAYDOWN MUST BE ENCLOSED BY CONSTRUCTION FENCING, AND THE AREAS DISTURBED BY THE STAGING AND LAYDOWN WORK MUST BE RESTORED TO THE EXISTING CONDITION OR BETTER, WITH THE CONTRACTOR REMOVING ANY MATERIALS USED TO MANAGE THE STAGING AREA AND PROVIDING SUITABLE SOIL AND SEEDING SATISFACTORY TO THE LABORATORY IN THE AREA AFTER ALL TEMPORARY WORK HAS BEEN REMOVED.
8. CONTRACTOR TO SUBMIT A FINAL SITE STAGING AND LOGISTICS TO ARGONNE PLAN FOR REVIEW PRIOR TO CONSTRUCTION. ALL SITE STAGING, CONSTRUCTION TRAILERS AND CONTRACTOR PARKING TO BE WITHIN LIMITS OF CONSTRUCTION FENCE.

GRAPHIC SCALE
(IN FEET)
1 inch = 30 ft.

LEGEND AND ABBREVIATIONS:

- TEMPORARY CONCRETE WALK
- TEMPORARY PARKING/LOADING AREA
- CONSTRUCTION ENTRANCE
- X — CONSTRUCTION FENCE
- SILT FENCE
- PROVIDE SEDIMENT BARRIER
- TEMPORARY SEDIMENT TRAP
- APCF — ADVANCED PROTEIN CRYSTALLIZATION FACILITY
- TYP — TYPICAL

SMITHGROUP
architecture engineering interiors planning
SMITHGROUP, INC
35 EAST WACKER
SUITE 2200
CHICAGO, IL 60601
T 312.641.0770
F 312.641.6728
www.smithgroup.com

JJR
landscape architecture planning urban design civil engineering environmental science
JJR, LLC
35 EAST WACKER DRIVE
SUITE 2200
CHICAGO, ILLINOIS 60601
312.641.0510 T
312.641.0668 F
www.jjr-us.com

AEI Affiliated Engineers
Affiliated Engineers, Inc.
5802 Research Park Boulevard
Madison, Wisconsin 53719
Tel 608.238.2616 Fax 608.238.2614

Thornton Tomasetti
Thornton Tomasetti, Inc.
330 N. Wabash Avenue, Suite 1500
Chicago IL 60611-7622
T 312.596.2000 F 312.596.2001

TERRA ENGINEERING LTD.
225 West Ohio Street, 4th Floor
Chicago, Illinois 60654
T:(312)467-0123 F:(312) 467-0220

SEALS AND SIGNATURES

JAMIL BOU-SAAB
062-047537
REGISTERED PROFESSIONAL ENGINEER OF ILLINOIS

KEYPLAN



REV. NO.	DESCRIPTION	BY	APVD	DATE
0	ISSUED FOR CONSTRUCTION			07/03/12

Argonne NATIONAL LABORATORY

FMS
Facilities Management Services

PROJECT TITLE: ADVANCED PROTEIN CRYSTALLIZATION FACILITY, ARGONNE NATIONAL LABORATORY

PROJECT NO: 22378.000

DRAWING TITLE

SITE STAGING PLAN

DESIGNED KM	A/E CADD FILE	FACILITY NO(S)
DRAWN AC/CM	A/E DWG. NO.	
CHECKED KS	CAD NO:	
PROJECT MANAGER ANL - JESSE ADAMS DATE - 07.03.2012	DWG STATE	
	BIND ORDER	

BENCHMARK #2 N: 50042.5469 E: 31031.7017 UPS 3 735.20

FACILITY DOCUMENT NUMBER: J446-101-W-C0.0.3

REV. NO.

Plot Date:
